
Chapter 8 — Execution roadmap and launch checklist

Owners: **F** founder · **E** engineering · **O** operations · **L** lawyer · **CA** chartered accountant.

8.1 Timeline

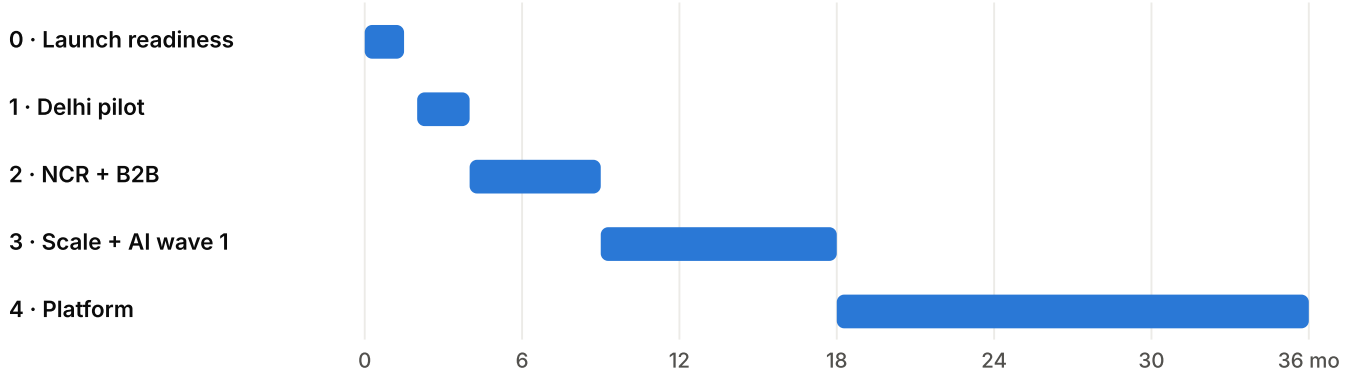

Months from go-ahead. Phases overlap slightly in practice; exit criteria, not dates, decide when the next phase starts.

8.2 Phase 0 — Launch readiness (weeks 0–6)

Business and legal

- [ ] Incorporate a private limited company; PAN, TAN, bank account (F, CA)
- [ ] GST registration; confirm SAC/rate per service and principal vs. marketplace model (CA)
- [ ] Trademark search and filing for the brand, classes 39 and 9/42 (L)
- [ ] Lawyer review of Terms, Privacy, Cancellation & Refund, Grievance, Cookie notice and both partner agreements (L)
- [ ] Appoint and publish the Grievance Officer (F)
- [ ] Insurance: commercial general liability and cyber; partner insurance requirements finalised (F)
- [ ] IP assignment agreements from all contributors (L)
- [ ] DPIIT Startup India recognition (optional, F)

Product and engineering (PRD v1.1 items L1–L11)

- [ ] Consent capture at booking and partner sign-up (E)
- [ ] Grievance officer settings fields and page (E)
- [ ] Partner KYC document upload and verification, with expiry blocking (E)
- [ ] Analytics consent banner (E)
- [ ] Contract template v2 with softened e-signature wording (L, E)
- [ ] Sentry, uptime monitor, log drain with 180-day retention (E)
- [ ] CI with type-check and tests (E)
- [ ] Production SMTP (SPF/DKIM), DLT SMS (MSG91) live, `EXPOSE_DEV_OTP=false`, rotate `AUTH_SECRET` and `CRON_SECRET` (E)
- [ ] Paid or self-hosted geocoding and routing before marketing spend (E)
- [ ] Load test: 50 concurrent bookings and 200 online drivers (E)

- [ ] Security review against `docs/developer/SECURITY.md` (E)

Operations

- [ ] Recruit and onboard 30+ partners across launch zones, with at least 3 night-capable trucks per zone (O)
- [ ] Staff the 24×7 desk (5 people, 3 shifts); train on `docs/operations/OPERATIONS-SOP.md` (O)
- [ ] Set rate cards, service areas, contact numbers and business details in Admin → Settings (O)
- [ ] Run 20 internal test bookings end to end, including night, cancellation and cash flows (O, E)

Exit criteria: every box above ticked; legal sign-off received; 30 active partners.

8.3 Phase 1 — Delhi pilot (months 2–4)

- Soft launch in 4 zones; Google Business Profile; SEO; small night-time paid search test.
- Weekly KPI review (chapter 7 table); fix the top three issues each week.
- Razorpay KYC and test mode; enable live mode once refunds (L10) ship.
- Collect the six pilot assumptions in chapter 6 §6.6.
- **Exit:** ≥ 30 jobs/day; p50 arrival < 35 min; completion > 90 %; rating ≥ 4.5; 100 % grievances acknowledged in 48 h.

8.4 Phase 2 — NCR and B2B (months 4–9)

- Open Noida, Gurugram, Ghaziabad and Faridabad in demand order (`coming_soon_lead`).
- B2B: accounts, API keys, status webhooks, monthly invoicing; sign 2+ contracts (dealers, fleets, an RSA company).
- Operator SaaS beta for 20 partners; push notifications; automated payouts; damage-claim workflow; photo condition report.
- Raise the seed round on pilot data.
- **Exit:** 150+ jobs/day; 2 B2B contracts live; CAC < ₹300 blended.

8.5 Phase 3 — Scale and AI wave 1 (months 9–18)

- AI-3 smart dispatch, AI-2 photo triage with AI-9 claim pack, AI-1 WhatsApp/voice agent, AI-8 support copilot.
- DPDP readiness by 13 May 2027: consent records, deletion/export, breach process, processor contracts.
- Second metro (choose by partner interest and demand data).
- Realtime (SSE/WebSockets) and Redis for locations; PostGIS for matching.
- **Exit:** 400+ jobs/day; contribution margin positive after marketing.

8.6 Phase 4 — Platform (months 18–36)

- RSA membership launch; insurer/OEM integrations; telematics pilots (AI-10).
- Three or more cities; per-city pricing and dispatch settings.
- **Exit:** EBITDA positive (chapter 6 planning case, year 3).

8.7 Engineering estimate for Phase 0 items

Item	Estimate (engineer-days)
Consent capture + records table	2
Grievance officer settings + page	0.5
KYC document upload (object storage, admin review, expiry blocking)	5
Analytics consent banner	1
Contract template v2	0.5
Monitoring, log drain, uptime	1.5
CI pipeline	0.5
Production integrations (SMTP, DLT, secrets)	1.5
Geocoding/routing provider switch or self-host	2–4
Load test + fixes	3
Security review + fixes	2
Total	**≈ 20–22 engineer-days** (about 2 weeks for 2 engineers)
